

2025 Procurement Performance

Where portfolio savings hide concentrated project, supplier, and delivery risk

The portfolio average is healthy—but it masks three decision-critical pockets

Portfolio result

-\$13.41M

Net under budget across 400 validated transactions. The result is real—but it is not evenly distributed.

Where leaders should look next

- 01 Three projects are net over budget
- 02 Three suppliers repeatedly price above budget
- 03 Delivery reliability falls to 64.29% in Finishing

The evidence passed every acceptance test before analysis began

The official dataset contains 400 distinct transactions. Instructor-approved corrections are logged at cell level; financial identities, dates, counts, totals, and Q1–Q4 were independently verified.

400

validated transactions


31 / 31

acceptance tests passed

83 / 83

independent Q1–Q4 matches

Only three projects are net over budget; all categories remain net under

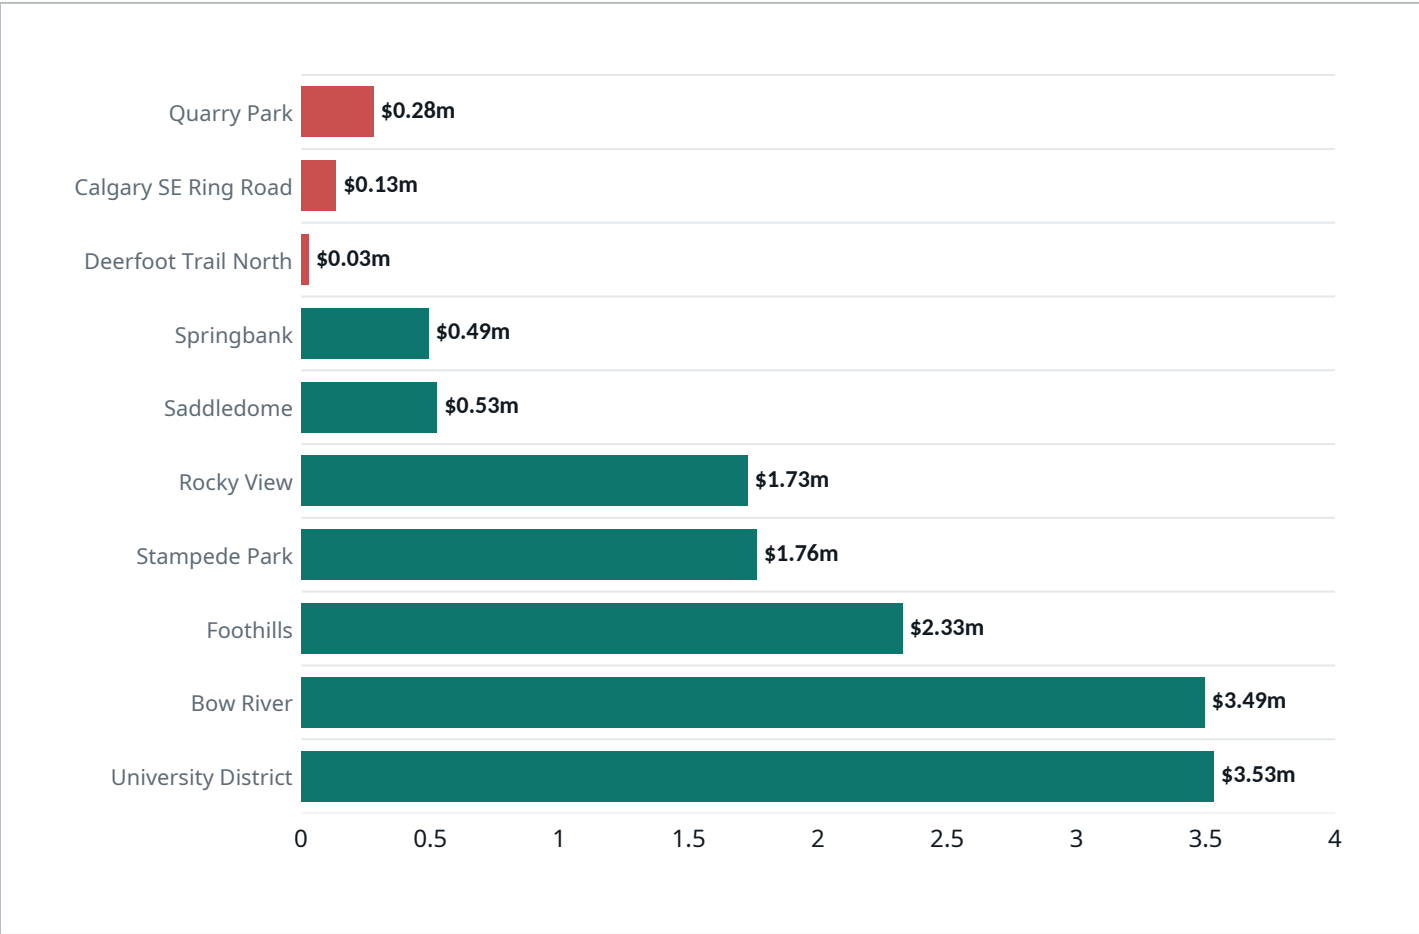

Ranked by summed Cost Variance (CAD).
Red = over budget; teal = under budget.
Bar length shows absolute size.


\$279.7K

Quarry Park ranks first

Calgary SE Ring Road: +\$134.6K
Deerfoot Trail North: +\$29.1K

Finishing is the closest category to zero at – \$60.0K.

Three suppliers show repeatable above-budget pricing

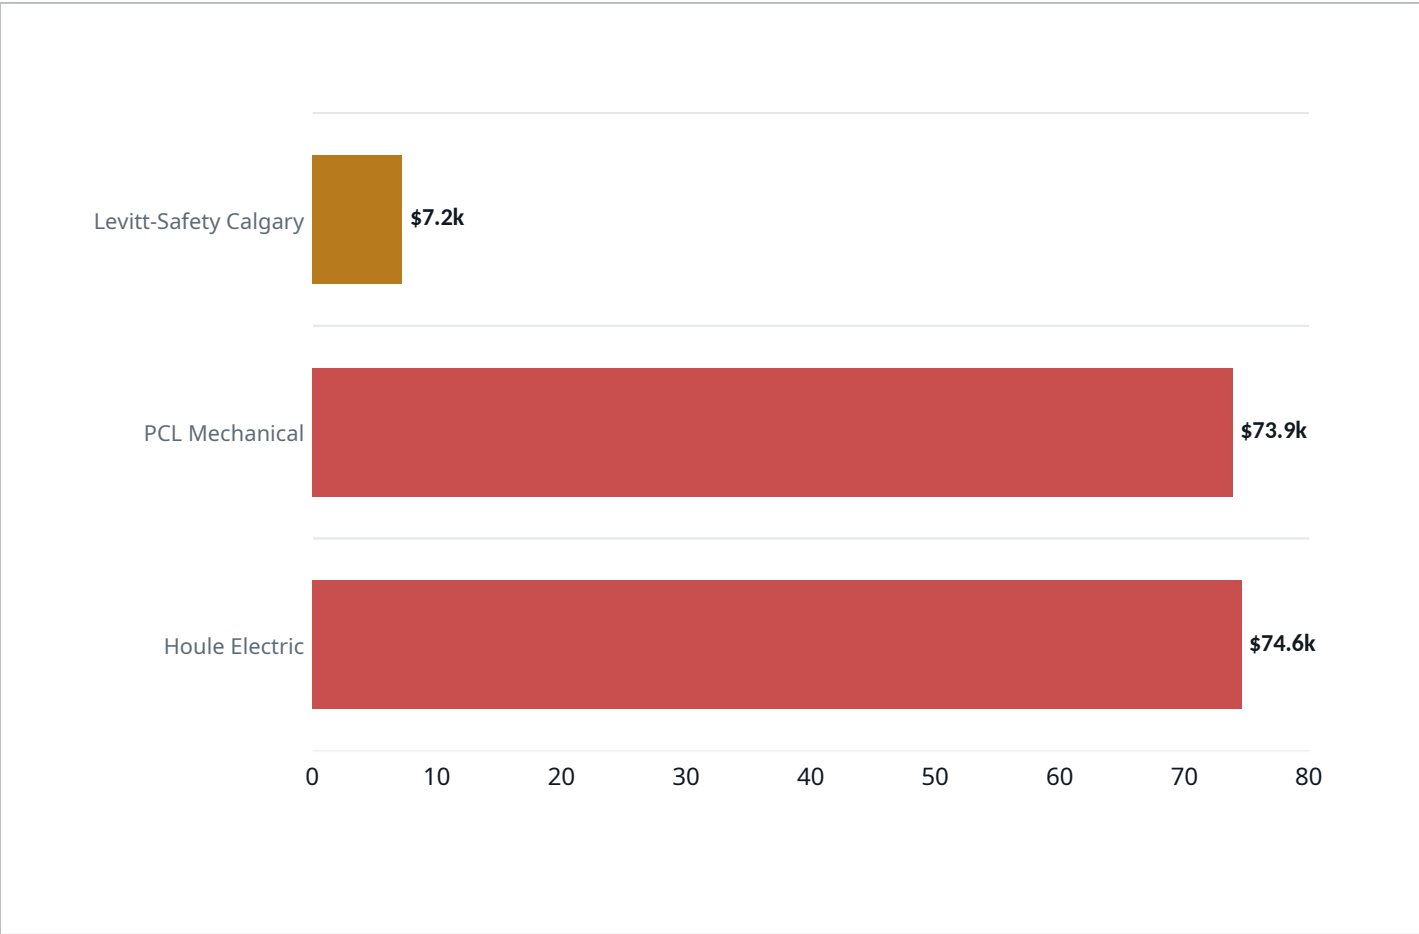


Consistently = more than 50% of orders over budget and positive total supplier variance.

\$2.02M
combined net positive variance

Houle: 63.64% above budget
PCL Mechanical: 53.33%
Levitt-Safety: 61.54%

Procurement method explains virtually none of the variance

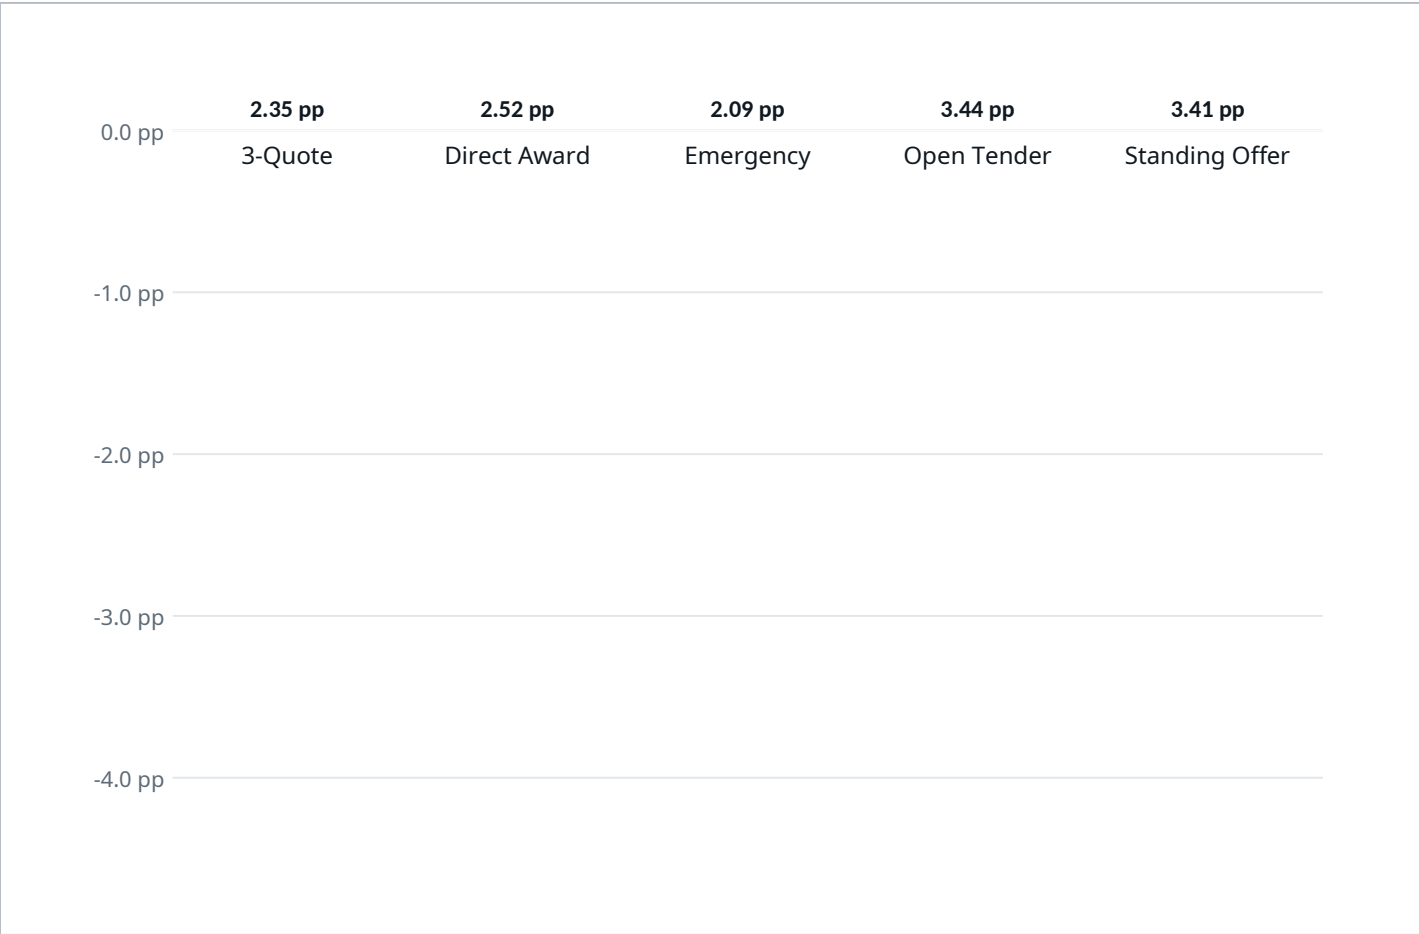

All five observed methods are under budget on average. Their distributions overlap heavily.


p = 0.894

ANOVA on row Variance_%

$\eta^2 = 0.0028$

≈0.28% of differences explained

Delivery reliability lags in Finishing and selected suppliers

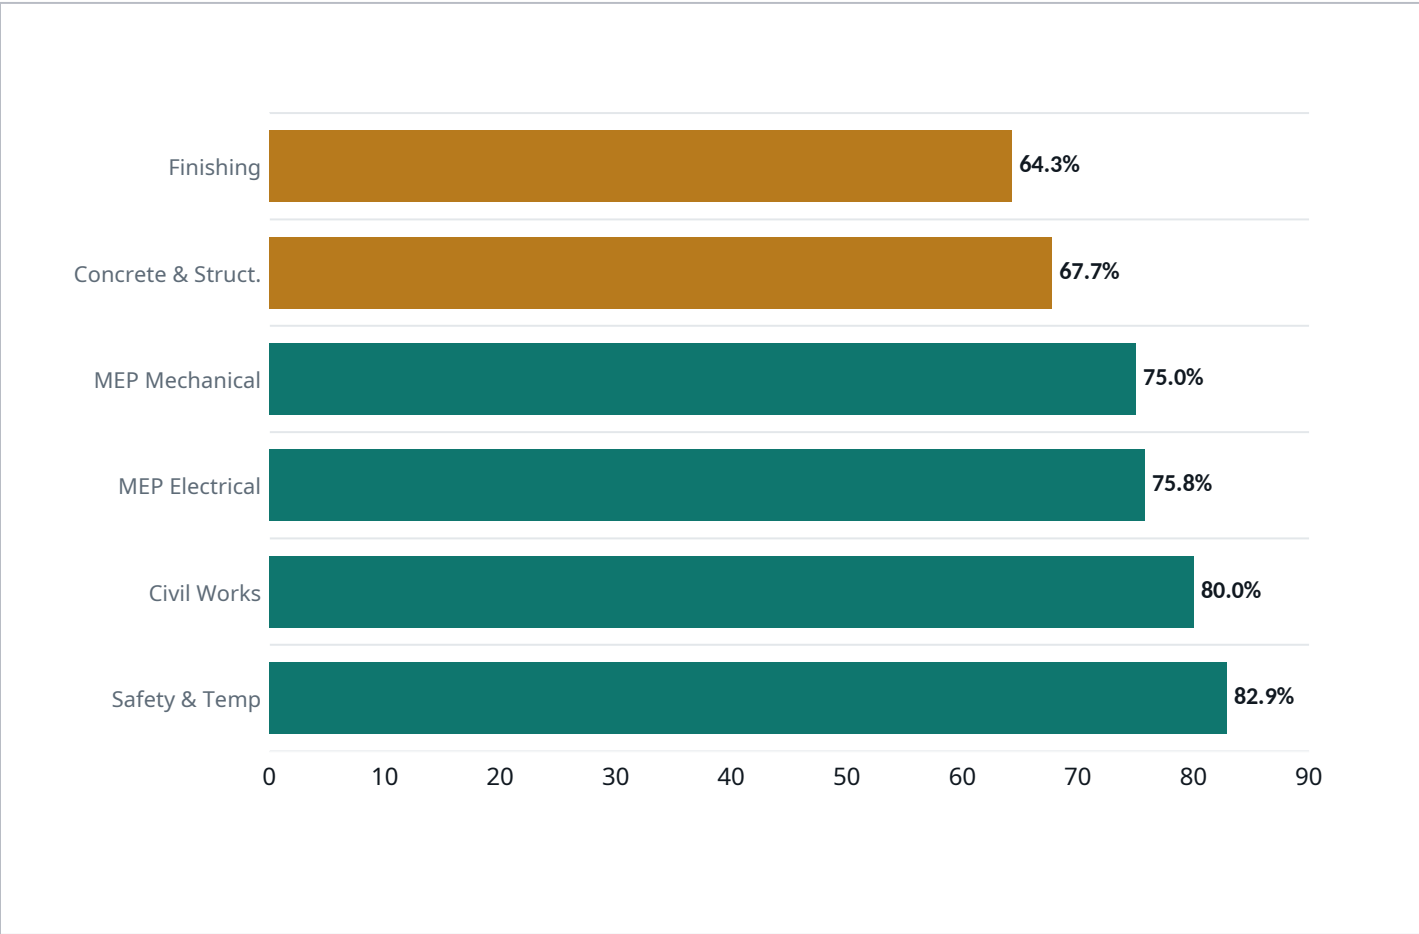

151 of 204 Delivered orders arrived on time. Pending, Cancelled, and Partially Delivered orders are excluded.

74.02%

portfolio on-time rate

Best category: Safety & Temp Works, 82.86%
Worst category: Finishing, 64.29%
Worst supplier: Tremco, 42.86%

Focus action where the same risk repeats

01

Launch targeted commercial reviews with the suppliers that meet the consistently-above-budget rule.

3 suppliers qualify: Houle Electric, PCL Mechanical, Levitt-Safety Calgary. Their combined net positive variance is \$2,022,856.51.

\$1.01M scenario

02

Add pre-award variance thresholds and monthly exception reviews for the three projects with positive net cost variance.

3 projects are net over budget: Quarry Park Mixed-Use Development, Calgary SE Ring Road Extension, Deerfoot Trail Widening - North. Combined net overrun is \$443,408.60.

\$221.7K scenario

03

Create supplier delivery scorecards and corrective-action plans for material categories and suppliers below the Delivered-only portfolio benchmark.

The Delivered-only on-time rate is 74.02%. 2 material categories are below that benchmark.

≈7 more on-time deliveries

Use the findings decisively—with four guardrails

What the data does not prove

- The analysis covers 2025 only
- Method comparisons are observational, not causal
- Imputed lead times affect two Civil Works records
- Recommendation impacts are directional, overlapping scenarios

What to do in the next 90 days

0–30 days

Launch supplier reviews and assign project thresholds

31–60 days

Publish delivery scorecards by supplier and category

61–90 days

Review exceptions, measure movement, and reset targets

**Act where risk repeats—not
where the portfolio average
looks comfortable.**

Target three suppliers · Protect three projects · Raise delivery reliability

Validated release · 31/31 acceptance tests passed
